


**WUNM-TV TRANSITION SCHEDULE AS OF OCTOBER 4, 2019**  
**FOR INTERNAL AND FCC STAFF USE; SUBJECT TO REVISION AND UPDATE WITHOUT NOTICE**

ID	Task Mode	Task Name	Duration	Start	Finish	3rd Quarter			4th Quarter			1st Quarter			2nd Quarter			3rd Quarter			4th Quarter			1st Quarter			2nd Quarter			3rd Quarter		
						Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug		
1	→	<b>WUNM-TV Repack Transition</b>	<b>96.8 wks</b>	<b>Mon 9/3/18</b>	<b>Fri 7/10/20</b>																											
2	✓ →	<b>Infrastructure Implementation</b>	<b>30 wks</b>	<b>Mon 9/3/18</b>	<b>Fri 3/29/19</b>																											
11	→	<b>Phase 1 Construction</b>	<b>37.8 wks</b>	<b>Wed 3/20/19</b>	<b>Mon 12/9/19</b>																											
12	✓ →	Infrastructure Construction	20 wks	Wed 3/20/19	Tue 8/6/19																											
13	✓ →	Remove Auxiliary Transmitter	5 days	Tue 7/9/19	Mon 7/15/19																											
14	✓ →	Main transmitter Installation	23 days	Mon 7/8/19	Wed 8/7/19																											
15	→	Main antenna Install	18 days	Thu 11/14/19	Mon 12/9/19																											
16	→	<b>Phase 2 Construction</b>	<b>3.8 wks</b>	<b>Mon 12/9/19</b>	<b>Thu 1/2/20</b>																											
17	→	Infrastructure Construction - Pha 2	2 wks	Mon 12/9/19	Fri 12/20/19																											
18	→	Auxiliary Transmitter Installation	14 days	Mon 12/16/19	Thu 1/2/20																											
19	→	<b>Transition Requirements</b>	<b>39 wks</b>	<b>Fri 6/7/19</b>	<b>Fri 3/6/20</b>																											
20	✓ →	Medical & MVPD Notifications	0 wks	Fri 6/7/19	Fri 6/7/19																											
21	✓ →	FCC CP Extension Filing Deadline	0 wks	Mon 6/10/19	Mon 6/10/19																											
22	✓ →	Transition Report	0 wks	Fri 6/28/19	Fri 6/28/19																											
23	→	Viewer Education	4.7 wks	Mon 11/4/19	Thu 12/5/19																											
24	→	Transition Date	0 wks	Fri 12/6/19	Fri 12/6/19																											
25	→	Transition Report	0 wks	Fri 12/13/19	Fri 12/13/19																											
26	→	<b>FCC CP Deadline</b>	<b>0 wks</b>	<b>Fri 3/6/20</b>	<b>Fri 3/6/20</b>																											
27	→	<b>Project Completion Deadline</b>	<b>0 wks</b>	<b>Fri 7/10/20</b>	<b>Fri 7/10/20</b>																											

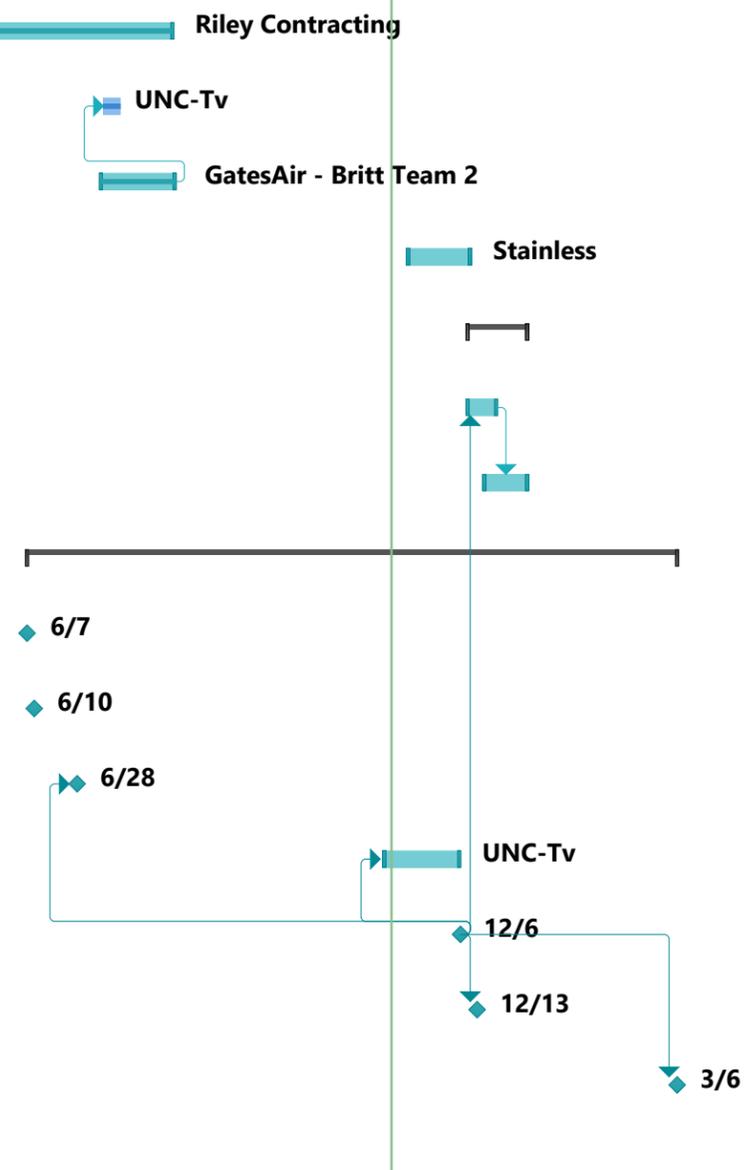

Project: WUNM-TV Schedule Date: Thu 11/7/19	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			
