


						September					October					November					D
						8/21	8/28	9/4	9/11	9/18	9/25	10/2	10/9	10/16	10/23	10/30	11/6	11/13	11/20	11/27	
ID	📌	Task Name	Duration	Start	Finish	Predecessors															
1		Channel 34 installation Sched	56 days	Fri 9/9/05	Fri 11/25/05																
2		Transmitter purchase	53 days	Fri 9/9/05	Tue 11/22/05																
3	📌	Transmitter delivery	6 wks	Fri 9/9/05	Thu 10/20/05																
4		Transmitter installation	1 wk	Mon 11/14/05	Fri 11/18/05	3,23															
5		Transmitter Proof	2 days	Mon 11/21/05	Tue 11/22/05	4															
6																					
7		Antenna purchase	22 days	Fri 9/9/05	Mon 10/10/05																
8	📌	Antenna delivery	4 wks	Fri 9/9/05	Thu 10/6/05																
9		Antenna installation	2 days	Fri 10/7/05	Mon 10/10/05	8															
10																					
11		Line purchase	14 days	Fri 9/30/05	Wed 10/19/05																
12		Line delivery	2 wks	Fri 9/30/05	Thu 10/13/05																
13		Line installation	4 days	Fri 10/14/05	Wed 10/19/05	12															
14																					
15		Final Check out	3 days	Wed 11/23/05	Fri 11/25/05																
16		Sweep antenna & line	2 days	Wed 11/23/05	Thu 11/24/05	9,13,5															
17		Sign-on	1 day	Fri 11/25/05	Fri 11/25/05	16															
18																					
19		Building purchase	33 days	Mon 10/3/05	Wed 11/16/05																
20	📌	Building delivery	21 days	Mon 10/3/05	Mon 10/31/05																
21		site prep	5 days	Tue 11/1/05	Mon 11/7/05	20															
22		set building	1 day	Tue 11/8/05	Tue 11/8/05	21															
23		Electrical installation	3 days	Wed 11/9/05	Fri 11/11/05	22															
24		Air Conditioning instal	3 days	Mon 11/14/05	Wed 11/16/05	23															



Project: Channel 34 project
Date: Fri 9/30/05

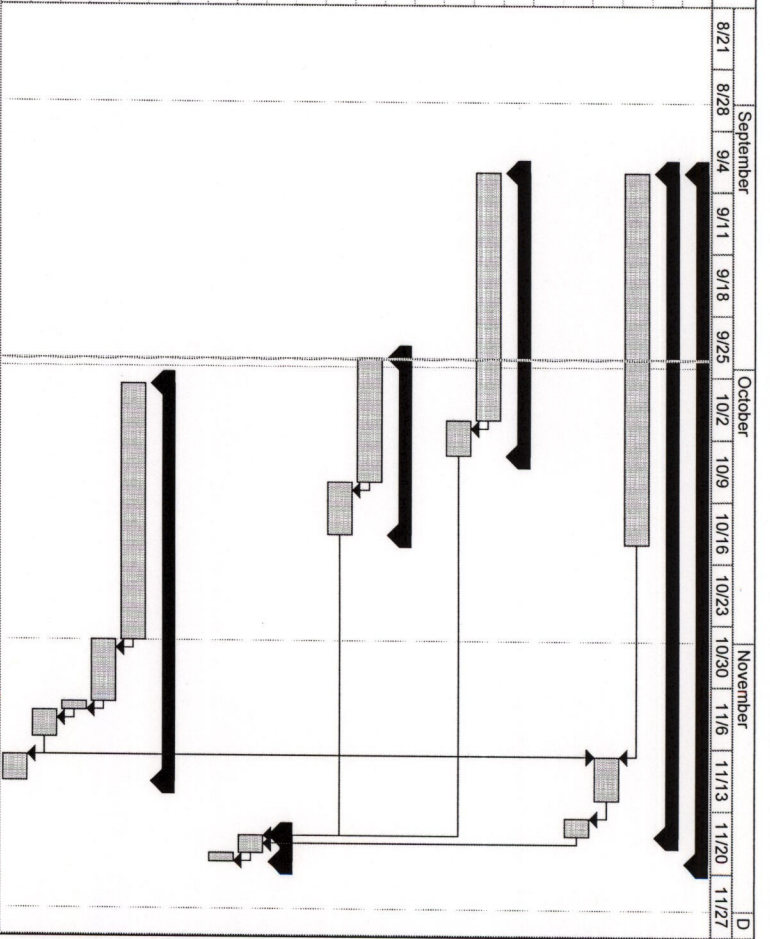
