


ID	Task Name	Duration	Start	Finish	Predecessors	September					October			November					D						
						8/21	8/28	9/4	9/11	9/18	9/25	10/2	10/9	10/16	10/23	10/30	11/6	11/13		11/20	11/27				
1	Channel 34 installation Sched	56 days	Fri 9/9/05	Fri 11/25/05																					
2	Transmitter purchase	53 days	Fri 9/9/05	Tue 11/22/05																					
3	Transmitter delivery	6 wks	Fri 9/9/05	Thu 10/20/05																					
4	Transmitter installation	1 wk	Mon 11/14/05	Fri 11/18/05	3,23																				
5	Transmitter Proof	2 days	Mon 11/21/05	Tue 11/22/05	4																				
6																									
7	Antenna purchase	22 days	Fri 9/9/05	Mon 10/10/05																					
8	Antenna delivery	4 wks	Fri 9/9/05	Thu 10/6/05																					
9	Antenna installation	2 days	Fri 10/7/05	Mon 10/10/05	8																				
10																									
11	Line purchase	14 days	Fri 9/30/05	Wed 10/19/05																					
12	Line delivery	2 wks	Fri 9/30/05	Thu 10/13/05																					
13	Line installation	4 days	Fri 10/14/05	Wed 10/19/05	12																				
14																									
15	Final Check out	3 days	Wed 11/23/05	Fri 11/25/05																					
16	Sweep antenna & line	2 days	Wed 11/23/05	Thu 11/24/05	9,13,5																				
17	Sign-on	1 day	Fri 11/25/05	Fri 11/25/05	16																				
18																									
19	Building purchase	33 days	Mon 10/3/05	Wed 11/16/05																					
20	Building delivery	21 days	Mon 10/3/05	Mon 10/31/05																					
21	site prep	5 days	Tue 11/1/05	Mon 11/7/05	20																				
22	set building	1 day	Tue 11/8/05	Tue 11/8/05	21																				
23	Electrical installation	3 days	Wed 11/9/05	Fri 11/11/05	22																				
24	Air Conditioning instal	3 days	Mon 11/14/05	Wed 11/16/05	23																				

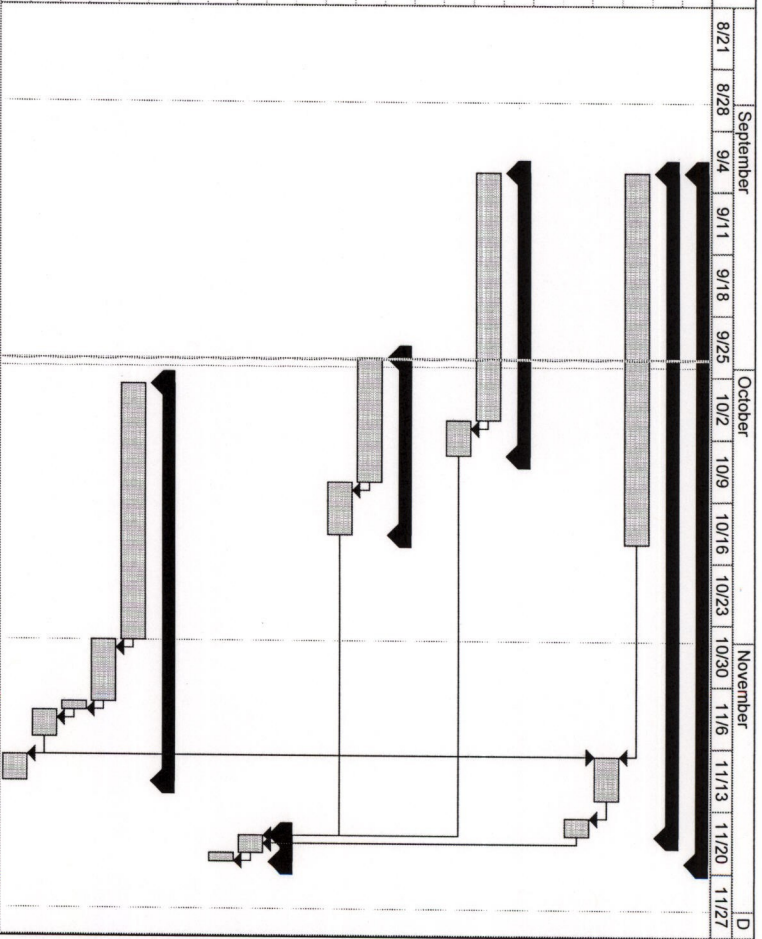

Project: Channel 34 project
Date: Fri 9/30/05

Task

Milestone

Split

Progress

◆

◆

◆

◆

Summary

Project Summary

External Tasks

External Milestone

Deadline

◆

◆

◆

◆

Summary

Project Summary

External Tasks

External Milestone

Deadline

◆

◆

◆

◆
