

Transmission System Proof of Performance Report

KLHY Kailua, HI

FIN: 767285

91.1 MHz

February, 19th 2023

TABLE OF CONTENTS

Introduction	3
Test Equipment	3
Station Equipment	3
Summary	3
Affidavit	4
Measurement Diagrams	5
Harmonic Emissions & Spurious Emissions Measurement Configuration.....	5
Measurement Results	6
Fundamental Frequency Measurement	6
Measurement Methodology	6
Harmonic Emissions Measurement.....	7
Intermodulation Emissions Measurements.....	7

Introduction

The permittee for the KLHY (file number 0000166864) construction permit is Educational Media Foundation. Stephen Wilde completed the KLHY transmitter and combiner proof of performance.

Test Equipment

- Agilent N9912A Spectrum Analyzer, Serial Number MY51464885
- AAT Directional Coupler
- Mini-Circuits High Pass filters
- 2-pole Bandpass Filters

Station Equipment

- FM Transmitter
- AAT Combiner System
- AAT FM Antenna System

Summary

Harmonics, Intermodulation, Spurious, and Occupied Bandwidth emissions measurements were completed at the output of the transmission network. The KLHY transmitter was operating at 100% power during the time of measurements. The measurements were completed in order to ensure compliance with the requirements of FCC Part 73.317.

Affidavit

STATE OF CALIFORNIA
Sacramento County


I, Stephen Wilde, do affirm that:

1. I have been engaged in the RF engineering and installation of broadcast facilities since 2005.
2. I hold a Bachelor of Science degree in Electrical Engineering from DeVry University Chicago, IL.
3. I further declare, under penalty of perjury, that the statements contained herein are true and correct to the best of my knowledge.

Stephen Wilde
SWE Services, LLC
February 19th 2023


X

Stephen Wilde



Measurement Diagrams

Harmonic Emissions & Spurious Emissions Measurement Configuration

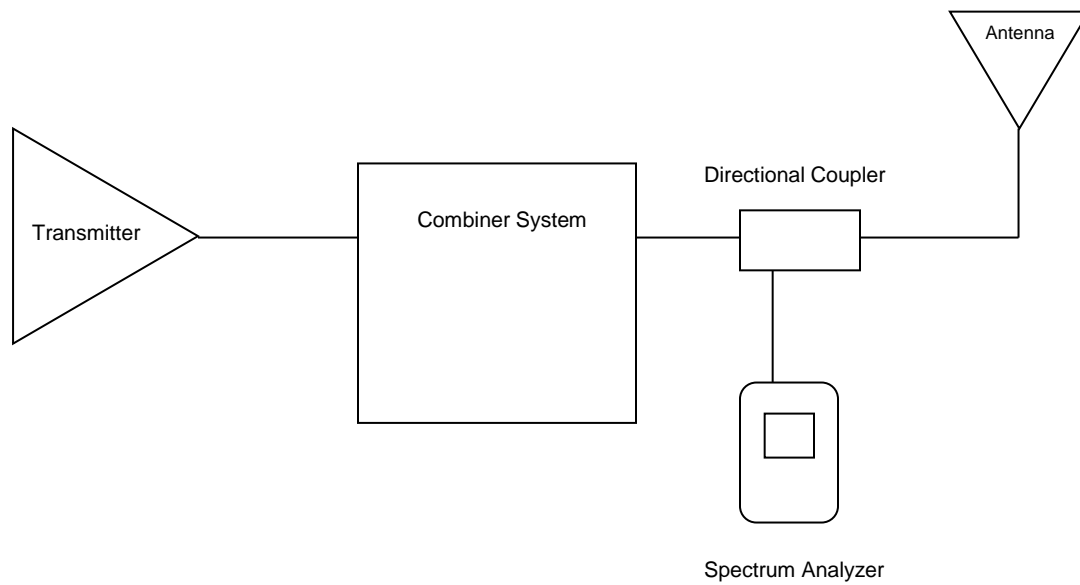

Measurement Results

Fundamental Frequency Measurement

Assigned Frequency	91.1000000	MHz	Variance in Hz
Measured Frequency	91.1000217	MHz	21.7

Measurement Methodology

To ensure accurate measurements, the frequency response of all couplers, RF filters, and sample ports were measured. The resulting dB characteristics were added to the recorded spectrum analysis measurements to ensure accurate calculations.

The test instrument reference point of the fundamental frequency is 0.13 dBm. The characteristics of the directional coupler forward sample-port is a dB reference relative to the fundamental frequency. Therefore, the directional coupler forward sample-port loss or gain, high pass filter loss, and dB reference point are added to the instrument measurement to provide the resulting dBc calculation.

Harmonic Emissions Measurement

Harmonic	Frequency (MHz)	Directional Coupler (dB)	High Pass Filter (dB)	Reference Level (dBm)	Instrument Reading (dBm)	Corrected Measurement (dBc)	FCC Limit (dBc)	Clearance (dB)
X2	182.20	-4.74	0.50	-0.13	-121.23	-125.60	-71.45	54.15
X3	273.30	-8.14	0.40	-0.13	-124.55	-132.42	-71.45	60.97
X4	364.40	-10.76	0.30	-0.13	-119.57	-130.16	-71.45	58.71
X5	455.50	-12.56	0.10	-0.13	-118.45	-131.04	-71.45	59.59
X6	546.60	-13.66	0.10	-0.13	-120.78	-134.47	-71.45	63.02
X7	637.70	-14.56	0.10	-0.13	-123.68	-138.27	-71.45	66.82
X8	728.80	-15.16	0.10	-0.13	-124.45	-139.64	-71.45	68.19
X9	819.90	-15.23	0.20	-0.13	-125.31	-140.47	-71.45	69.02

Intermodulation Emissions Measurements

The KLHY transmission circuit was analyzed using an Agilent N9912A spectrum analyzer while all combiner circuits operated at 100% power. The KLHY transmission circuit meets the intermodulation spurious emissions requirements.

IM Frequency (MHz)	Directional Coupler (dB)	Band Pass Filter (dB)	Reference Level (dBm)	Instrument Reading (dBm)	Corrected Measurement (dBc)	FCC Limit (dBc)	Clearance (dB)
87.7	0.00	0.00	-0.13	-98.63	-98.76	-71.45	27.31
97.9	0.00	0.00	-0.13	-94.55	-94.68	-71.45	23.23
