

# **Proof of Performance Report**

KGCL Jordan Valley, OR

FIN: 85777

90.9 MHz

September 1, 2019

## **TABLE OF CONTENTS**

|  |   |
|--|---|
| Introduction .....   | 3 |
| Test Equipment .....   | 3 |
| Station Equipment .....  | 3 |
| Summary .....  | 3 |
| Affidavit .....  | 4 |
| Measurement Diagrams .....   | 5 |
| Harmonic Emissions & Spurious Emissions Measurement Configuration..... | 5 |
| Measurement Results .....  | 6 |
| Fundamental Frequency Measurement .....                                | 6 |
| Measurement Methodology .....  | 6 |
| Harmonic Emissions Measurement.....                                    | 7 |
| Intermodulation Emissions Measurements.....                            | 7 |

## Introduction

The permittee for the KGCL Jordan Valley (file number BPED-20181127AAU) construction permit is Educational Media Foundation. Stephen Wilde completed the KGCL combiner proof of performance on September 1st 2019.

## Test Equipment

- Agilent N9912A Spectrum Analyzer, Serial Number MY51464885
- AAT Directional Coupler
- Mini-Circuits High Pass filters
- FM 2-Cavity Bandpass Filter

## Station Equipment

- Nautel 1 kW FM Transmitter
- AAT FM Combiner System
- PSI 4-bay FM Antenna

## Summary

Harmonics, Intermodulation, Spurious, and Occupied Bandwidth emissions measurements were completed at the output of the transmission network. The KGCL transmitter was operating at 100% power during the time of measurements. The measurements were completed in order to ensure compliance with the requirements of FCC Part 73.317.

Affidavit

STATE OF CALIFORNIA  
Sacramento County

I, Steve Wilde, do affirm that:

1. I have been engaged in the RF engineering and installation of broadcast facilities since 2005.
2. I hold Bachelor of Science degree in Electrical Engineering from DeVry University Chicago, IL.
3. I further declare, under penalty of perjury, that the statements contained herein are true and correct to the best of my knowledge.

Stephen Wilde  
SWE Services, LLC  
September 1st 2018

9/16/2019

X




---

Stephen Wilde

Signed by: Stephen Wilde

# Measurement Diagrams

## Harmonic Emissions & Spurious Emissions Measurement Configuration

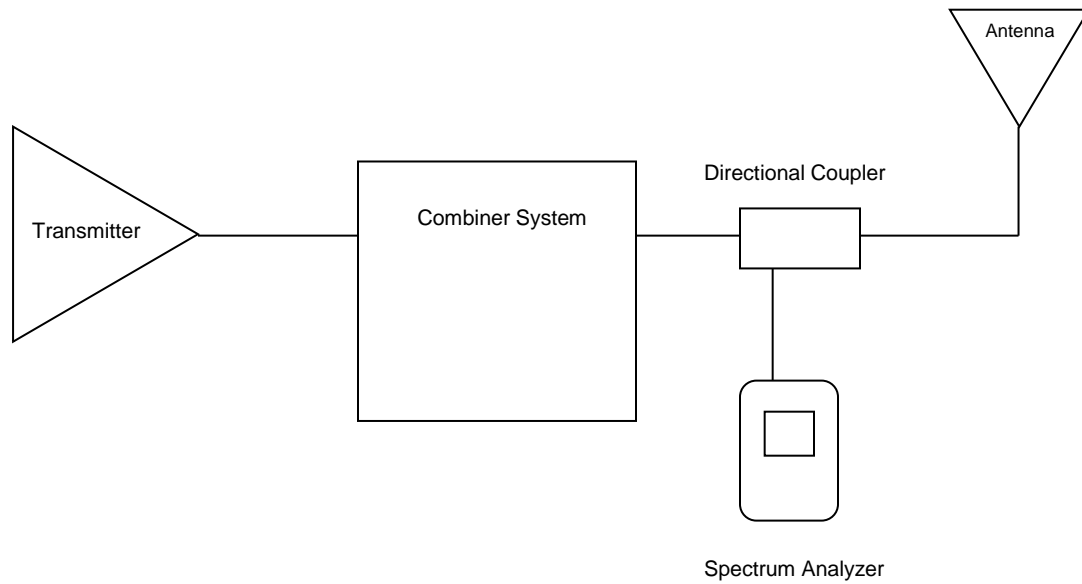

## Measurement Results

### Fundamental Frequency Measurement

|                    |            |     |                |
|--------------------|------------|-----|----------------|
| Assigned Frequency | 90.9000000 | MHz | Variance in Hz |
| Measured Frequency | 90.9001375 | MHz | 137.5          |

### Measurement Methodology

To ensure accurate measurements, the frequency response of all couplers, RF filters, and sample ports were measured. The resulting dB characteristics were added to the recorded spectrum analysis measurements to ensure accurate calculations.

The test instrument reference point of the fundamental frequency is 0.00 dBm. The characteristics of the directional coupler forward sample-port is a dB reference relative to the fundamental frequency. Therefore, the directional coupler forward sample-port loss or gain, high pass filter loss, and dB reference point are added to the instrument measurement to provide the resulting dBc calculation.

Harmonic Emissions Measurement

| Harmonic | Frequency (MHz) | Directional Coupler (dB) | High Pass Filter (dB) | Reference Level (dB) | Instrument Reading (dB) | Corrected Measurement (dBc) | FCC Limit (dBc) | Clearance (dB) |
|----------|-----------------|--------------------------|-----------------------|----------------------|-------------------------|-----------------------------|-----------------|----------------|
| X2       | 181.80          | 0.06                     | 0.50                  | 0.00                 | -105.00                 | <b>-104.44</b>              | -73.00          | <b>31.44</b>   |
| X3       | 272.70          | 1.26                     | 0.40                  | 0.00                 | -90.70                  | <b>-89.04</b>               | -73.00          | <b>16.04</b>   |
| X4       | 363.60          | 3.86                     | 0.30                  | 0.00                 | -103.90                 | <b>-99.74</b>               | -73.00          | <b>26.74</b>   |
| X5       | 454.50          | 6.66                     | 0.10                  | 0.00                 | -101.70                 | <b>-94.94</b>               | -73.00          | <b>21.94</b>   |
| X6       | 545.40          | 8.96                     | 0.10                  | 0.00                 | -104.60                 | <b>-95.54</b>               | -73.00          | <b>22.54</b>   |
| X7       | 636.30          | 11.16                    | 0.10                  | 0.00                 | -104.40                 | <b>-93.14</b>               | -73.00          | <b>20.14</b>   |
| X8       | 727.20          | 11.96                    | 0.10                  | 0.00                 | -106.70                 | <b>-94.64</b>               | -73.00          | <b>21.64</b>   |
| X9       | 818.10          | 13.26                    | 0.20                  | 0.00                 | -105.30                 | <b>-91.84</b>               | -73.00          | <b>18.84</b>   |

Intermodulation Emissions Measurements

The KGCL transmission circuit was analyzed using an Agilent N9912A spectrum analyzer while all combiner circuits operated at 100% power. The KGCL transmission circuit meets or exceeds the intermodulation spurious emissions requirements.

| IM Frequency (MHz) | Directional Coupler (dB) | Band Pass Filter (dB) | Reference Level (dB) | Instrument Reading (dB) | Corrected Measurement (dBc) | FCC Limit (dBc) | Clearance (dB) |
|--------------------|--------------------------|-----------------------|----------------------|-------------------------|-----------------------------|-----------------|----------------|
| 87.3               | 0.00                     | 0.00                  | 0.00                 | -85.03                  | <b>-85.03</b>               | -73.00          | <b>12.03</b>   |
| 92.7               | 0.00                     | 0.00                  | 0.00                 | -86.33                  | <b>-86.33</b>               | -73.00          | <b>13.33</b>   |
